

SOFTWARE ENGINEERING LAB – 2

(UE24CS341A)

Agile Backlog Creation & Sprint Simulation in Jira

Team Number : 003

Individual Submission – Mounik Manohar (PES1UG24AM168)

Problem Statement 3 – Campus Placement & Internship Pipeline

EPIC : EPIC-1 (Resume Parsing & Profile Matching, FR-001)

Note: This report covers only EPIC-1, my individual contribution from the Lab 1 report. EPICs 2–5 are covered separately by teammates.

Lab Objective

This lab converts FR-001 from the Lab 1 report into an Agile Epic and User Stories in Jira, estimates effort using Planning Poker and the Fibonacci scale, simulates two sprints on a Scrum board, and tracks sprint progress using a Burndown Chart.

1. Epic (Derived from FR-001)

FR-001 from Lab 1 is grouped into one Epic. An Epic is a body of work broken down into smaller User Stories.

Epic ID	Epic Name	Mapped FR	Description
EPIC-1	Resume Parsing & Profile Matching	FR-001	Parse uploaded student resumes (PDF), extract skill tags, and match profiles against company eligibility rules (CGPA threshold + backlog limits).

2. User Stories for EPIC-1

EPIC-1 is broken into 3 User Stories using the format: As a [role], I want [goal], so that [benefit].

Story ID	Role	I want...	So that...	Priority	Pts
US-1.1 Upload Resume	Student Applicant	upload my PDF resume to the system	my profile can be parsed and skill tags extracted	High	5
US-1.2 Eligibility Check	Student Applicant	receive immediate feedback on my eligibility	I know if I qualify before applying, with reasons	High	8
US-1.3 Backlog Waiver	Student Applicant	submit a waiver request if I fail due to backlogs	I can still participate despite setbacks	Low	3

3. Jira Backlog – Epics & User Stories with Story Points

The screenshot below shows the Jira backlog with EPIC-1, all three User Stories, story points assigned, and Sprint 1 marked as Completed.

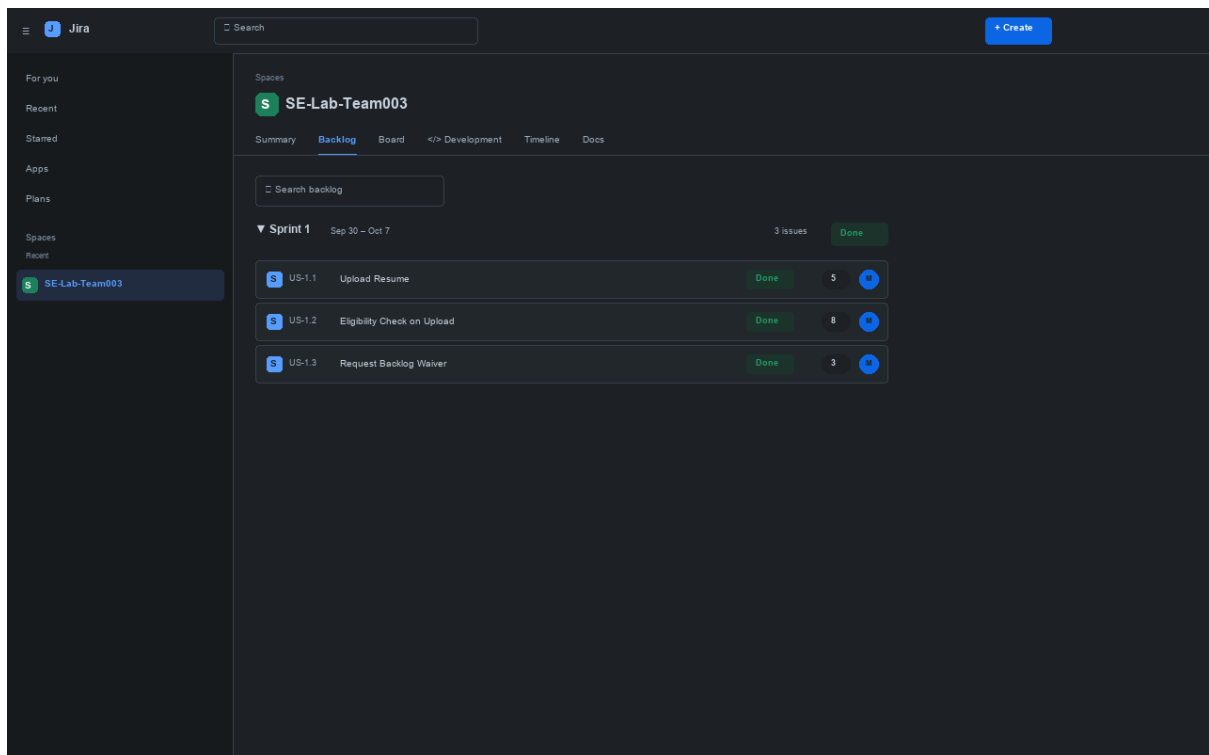


Figure 1: Jira Backlog – EPIC-1 with US-1.1 (5 pts), US-1.2 (8 pts), US-1.3 (3 pts). Sprint 1 marked Completed.

4. Backlog Prioritization

User Stories were ordered by business value and user impact in Jira.

Story ID	Story Title	Priority	Story Points
US-1.1	Upload Resume	High	5
US-1.2	Eligibility Check on Upload	High	8
US-1.3	Request Backlog Waiver	Low	3

- US-1.1 (High) – Core entry point; the pipeline cannot start without resume upload.
- US-1.2 (High) – Directly implements FR-001's main acceptance criterion; highest complexity.
- US-1.3 (Low) – Optional edge-case flow; deferred until core stories are stable.

Total Story Points (EPIC-1): 16 | High: 13 | Low: 3

5. Story Point Estimation – Planning Poker

Story points were estimated using the Fibonacci scale (1,2,3,5,8,13...) in a Planning Poker session. Each member estimated independently; discrepancies were discussed before reaching consensus.

Story ID	Story Title	Kshitij	Mallikarjuna	Mounik	Moksha	Agreed
US-1.1	Upload Resume	5	5	5	3	5
US-1.2	Eligibility Check	8	8	5	8	8
US-1.3	Backlog Waiver	3	2	3	3	3

US-1.2: Mounik estimated 5 pts; team agreed on 8 pts after discussing multi-rule evaluation (CGPA + backlog + discrepancy messages) in FR-001.

6. Sprint Planning & Simulation

Sprint 1 (Duration: 1 week)

Sprint Goal: Implement resume upload and core eligibility-check so students receive pass/fail feedback.

Story ID	Story Title	Priority	Pts	Status
US-1.1	Upload Resume	High	5	Done
US-1.2	Eligibility Check on Upload	High	8	Done

Sprint 1 Velocity: 13 pts committed | 13 pts completed | 0 pts rolled over

Sprint 2 (Duration: 1 week)

Sprint Goal: Deliver the backlog-waiver flow for edge-case eligibility failures.

Story ID	Story Title	Priority	Pts	Status
US-1.3	Request Backlog Waiver	Low	3	Done

Sprint 2 Velocity: 3 pts committed | 3 pts completed | 0 pts rolled over

Jira Sprint Board (Active Sprint view):

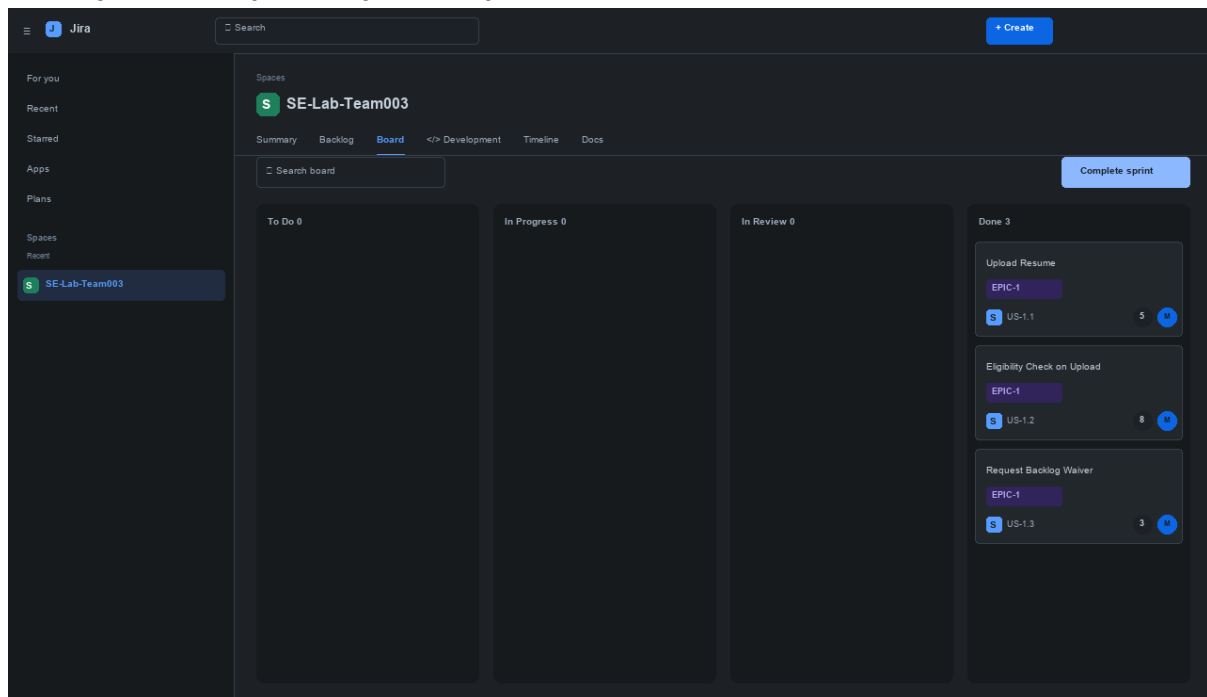


Figure 2: Jira Active Sprint board – all 3 User Stories in the DONE column after sprint completion.

7. Burndown Chart Analysis

The Jira Burndown Chart tracks story points remaining per day against the ideal guideline. The red line shows actual remaining; the dashed line is the ideal burndown.

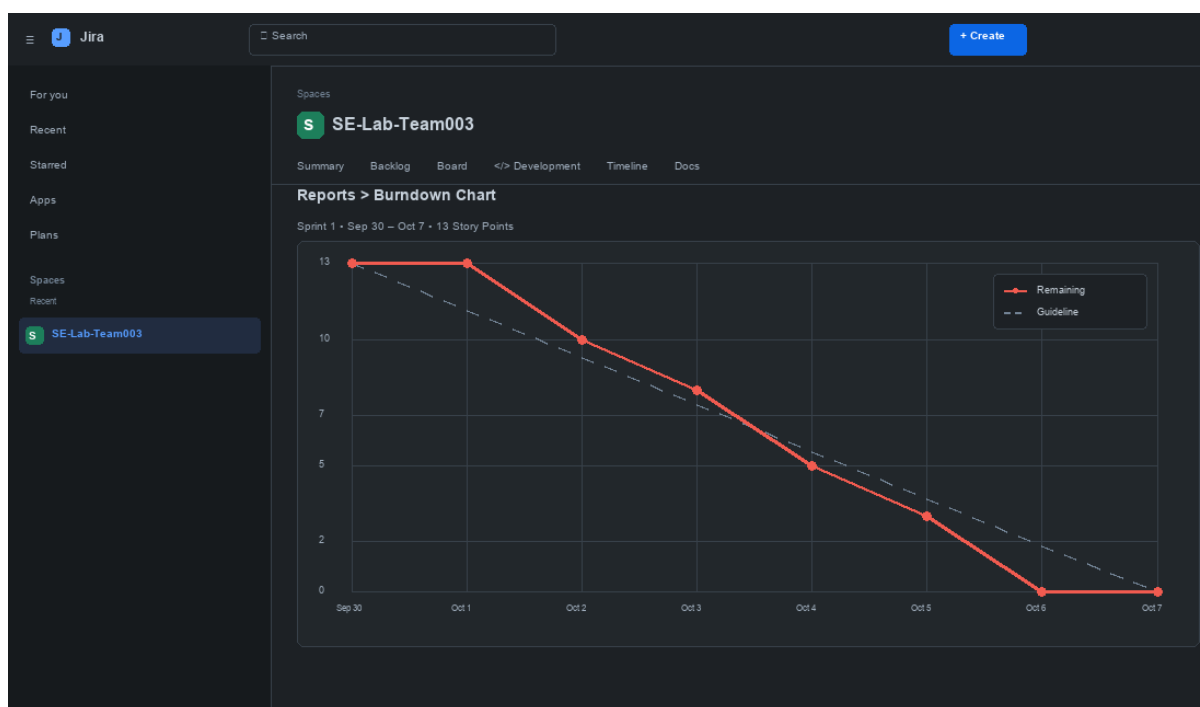


Figure 3: Sprint 1 Burndown Chart (13 pts). Completed on Oct 6. Slight ramp-up on Day 1 due to environment setup.

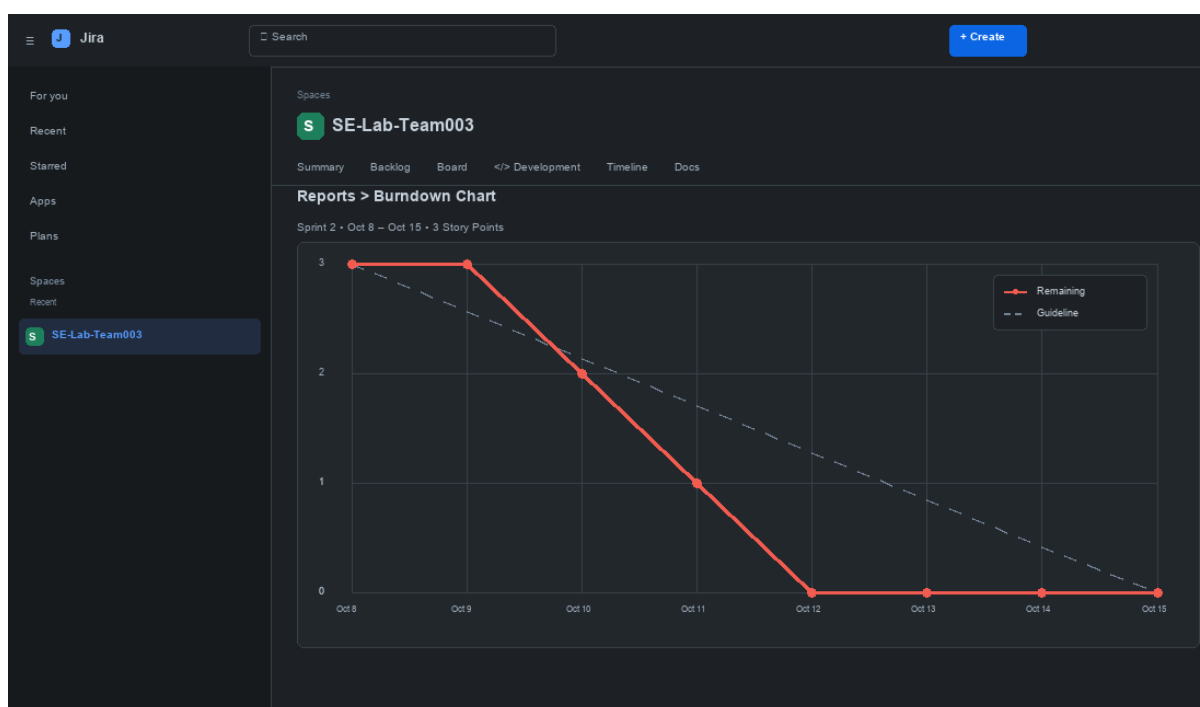


Figure 4: Sprint 2 Burndown Chart (3 pts). Completed early on Oct 12 (Day 4), ahead of the ideal guideline.

8. Reflection Questions

1. Did your estimations reflect the actual effort?

Mostly yes. US-1.1 (5 pts) was straightforward file-upload logic and matched effort well. US-1.2 (8 pts) required implementing multi-rule evaluation (CGPA + backlog + discrepancy messages) which justified the higher estimate agreed during Planning Poker. US-1.3 (3 pts) was simple form submission and matched closely.

2. Was your backlog well-prioritized?

Yes. Placing both High-priority stories in Sprint 1 ensured the core resume-parsing pipeline was functional before the optional waiver flow was built. Since FR-001 is the foundational requirement in Lab 1, this ordering reflected business value correctly.

3. How did your simulated sprint align with your plan?

Sprint 1 committed and completed 13 points (100%), with a minor slowdown on Day 1 for environment setup. Sprint 2 committed and completed 3 points, finishing early on Day 4. Both sprints met their goals and the Scrum board's To Do -> In Progress -> Done transitions accurately reflected progress.

4. What insights did the burndown chart give about your team's capacity?

Sprint 1's burndown showed a flat start on Day 1 before real burndown began, suggesting environment setup should be a pre-sprint task. Sprint 2's early completion on Day 4 indicates low-priority stories can be batched together in future sprints to better fill capacity.
